

ID	Task Name	Duration	Start	Finish	Nov 15, '20				Dec 13, '20				Jan 10, '21			
					10/25	11/1	11/8	11/15	11/22	11/29	12/6	12/13	12/20	12/27	1/3	1/10
1	MADISON	52 days	Mon 10/26/20	Tue 1/5/21												
2	Silt Fence	5 days	Mon 10/26/20	Fri 10/30/20												
3	Clearing / Dirt Cut	12 days	Mon 11/2/20	Tue 11/17/20												
4	Drainage	15 days	Wed 11/18/20	Tue 12/8/20												
5	Road Work	20 days	Wed 12/9/20	Tue 1/5/21												
6	UTILITIES	56 days	Wed 12/9/20	Wed 2/24/21												
7	Sewer	11 days	Wed 12/9/20	Wed 12/23/20												
8	Drainage	20 days	Thu 12/24/20	Wed 1/20/21												
9	Water	15 days	Thu 1/21/21	Wed 2/10/21												
10	Reclaim	10 days	Thu 2/11/21	Wed 2/24/21												
11	ROAD WORK	57 days	Thu 2/4/21	Fri 4/23/21												
12	Sub-Base	15 days	Thu 2/4/21	Wed 2/24/21												
13	Curb	15 days	Thu 2/25/21	Wed 3/17/21												
14	Limerock	15 days	Thu 3/18/21	Wed 4/7/21												
15	Finish Rock	15 days	Thu 4/1/21	Wed 4/21/21												
16	Asphalt	2 days	Thu 4/22/21	Fri 4/23/21												
17	FINAL WORK	13 days	Mon 4/26/21	Wed 5/12/21												
18	Final Grade	5 days	Mon 4/26/21	Fri 4/30/21												
19	Stripes / Signs	5 days	Mon 5/3/21	Fri 5/7/21												
20	Final Insp complete	3 days	Mon 5/10/21	Wed 5/12/21												

Project: Copper Phase 3
Date: Mon 10/5/20


Task Progress
Split

Milestone

Summary Project Summary

External Tasks External Milestone

Deadline

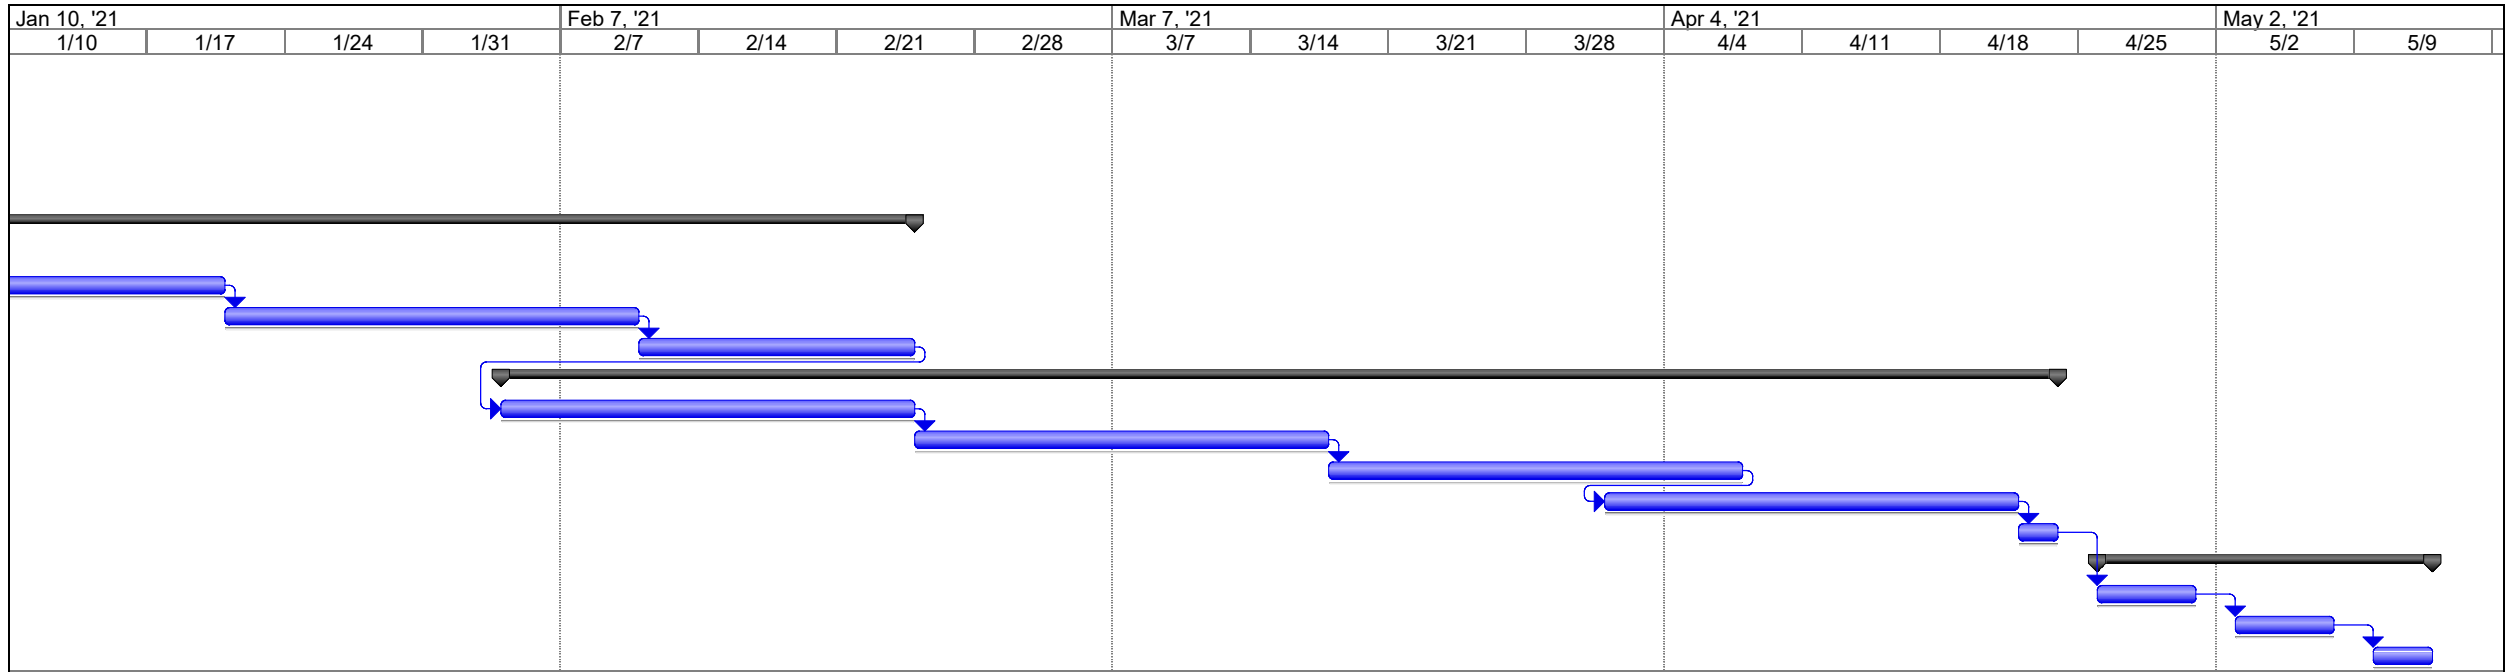

Project: Copper Phase 3
Date: Mon 10/5/20

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
